



City of Grand Island

Tuesday, February 22, 2005

Council Session

Item G10

#2005-48 - Approving Time Extension to Contract with The Diamond Engineering Company for Construction of Sanitary Sewer Districts No. 510 and 514

Staff Contact: Steven P. Riehle, Public Works Director

Council Agenda Memo

From: Steven P. Riehle, Public Works Director

Meeting: February 22, 2005

Subject: Approving Time Extension to the Contract with The Diamond Engineering Company for Construction of Sanitary Sewer Districts 510 and 514

Item #'s: G-10

Presenter(s): Steven P. Riehle, Public Works Director

Background

The City Council awarded the bid for construction of Sanitary Sewer Districts 510 and 515 to The Diamond Engineering Company on May 25, 2004. Diamond Engineering is requesting a time extension to complete the work for the above named district.

Discussion

The start of the project was delayed from an anticipated early start date of June 21, 2004 to August 16, 2004 because Right-of-Way was not acquired along the south side of 13th Street until the July 29, 2004 Council meeting. The start of the project was further delayed by a utility conflict with a Qwest junction box that was not moved until October 15, 2004. Work on the project started on September 7, 2004 and progressed satisfactorily up to where the Qwest junction box was relocated.

Alternatives

It appears that the Council has the following alternatives concerning the issue at hand. The Council may:

1. Make a motion to approve the time extension.
2. Refer the issue to a Committee.
3. Postpone the issue to a future date.
4. Take no action on the issue.

Recommendation

City Administration recommends that the Council extend the completion date for the project 58 working days for the days lost between June 21, 2004 and September 7, 2004.

Sample Motion

Move to approve the time extension.

POINT OF BEGINNING

PART OF S.W. 1/4, S.W. 1/4
SECTION 11-11-10


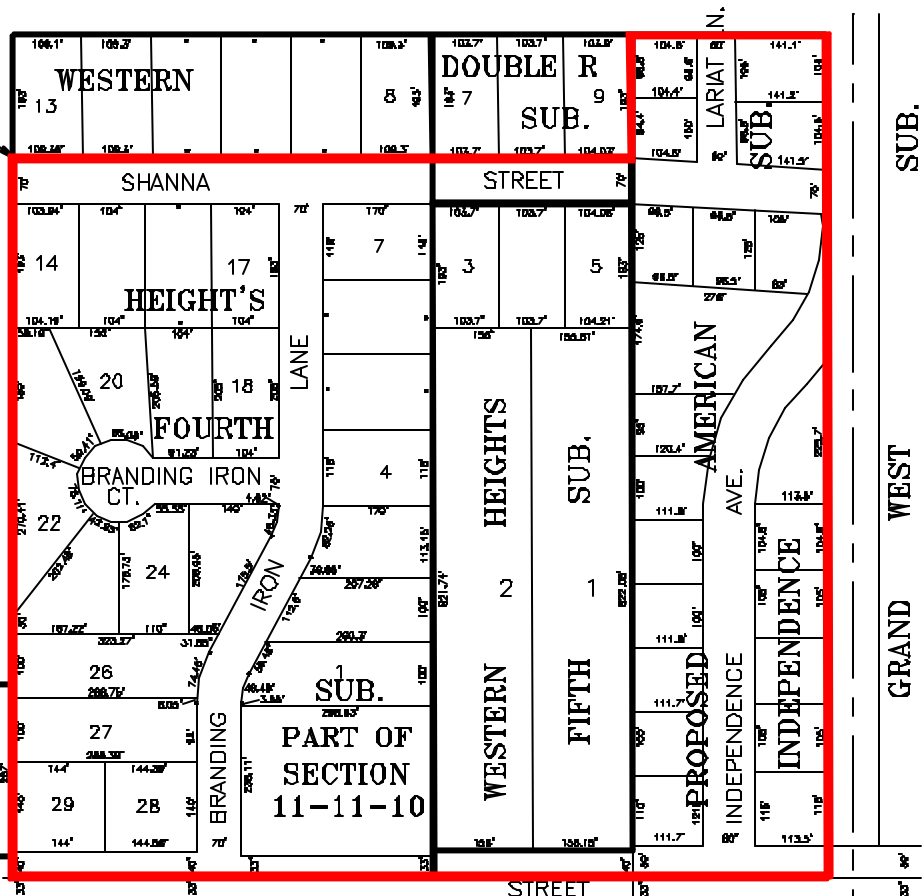


EXHIBIT "A"

SANITARY SEWER DISTRICT NO. 510





DATE: 7/14/03
DRN BY: L.D.C.
SCALE: 1"=300'

PLAT ACCOMPANY ORDINANCE
NO. 8826

PART OF S.W. 1/4, S.W. 1/4
SECTION 11-11-10

POINT OF BEGINNING

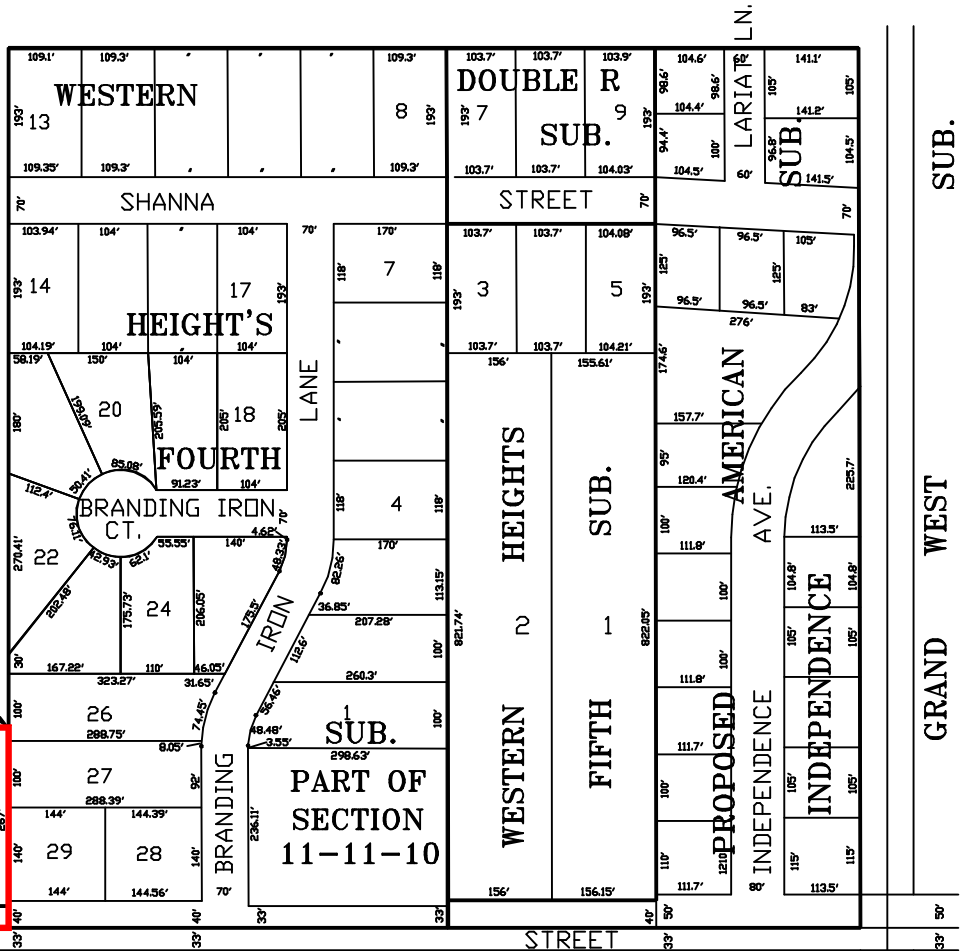

PART OF N.W. 1/4
SECTION 14-11-10



EXHIBIT "A"

SANITARY SEWER DISTRICT NO. 514

CITY OF
GRAND ISLAND
PUBLIC WORKS DEPARTMENT

DATE: 3/15/04
DRN BY: L.D.C.
SCALE: 1"=300'

PLAT ACCOMPANY ORDINANCE
NO. 8893

RESOLUTION 2005-48

WHEREAS, on May 25, 2004, by Resolution 2004-121, the City Council of the City of Grand Island approved the bid of The Diamond Engineering Company of Grand Island, Nebraska for Sanitary Sewer District Nos. 510 and 514 and Water Main District Nos. 443 and 447T; and

WHEREAS, the start of the project was delayed until right-of-way acquisitions were complete; and

WHEREAS, construction was also delayed for the relocation of a Qwest junction box; and

WHEREAS, it is requested that an extension of time be granted to The Diamond Engineering Company to complete such work; and

WHEREAS, it is recommended that the completion date for the project be extended 58 working days.

NOW, THEREFORE, BE IT RESOLVED BY THE MAYOR AND COUNCIL OF THE CITY OF GRAND ISLAND, NEBRASKA, that the completion date for Sanitary Sewer District Nos. 510 and 514 and Water Main District Nos. 443 and 447T is hereby extended 58 working days.

BE IT FURTHER RESOLVED, that the Mayor is hereby authorized and directed to execute such Contract Modification on behalf of the City of Grand Island.

- - -

Adopted by the City Council of the City of Grand Island, Nebraska, February 22, 2005.

RaNae Edwards, City Clerk

Approved as to Form	☐ _____
February 17, 2005	☐ City Attorney
